

<b>Weekly Water Report</b>	As of:	As of:	
	April 28, 2026	May 12, 2026	
<b>New Hogan (NHG) TOC</b>	<b>294,091</b>	<b>317,100*</b>	<b>AF</b>
Storage:	213,086	212,815*	AF
Net Storage Change:	+1,387	-271	AF
Inflow:	151	62*	CFS
Release:	115	128*	CFS
<b>New Melones (NML) Allocation</b>	<b>75,000</b>	<b>75,000</b>	<b>AF</b>
Storage:	1,870,734	1,872,010*	AF
Net Storage change:	+9,656	+1,276	AF
Inflow:	1,414	1,483*	CFS
Release:	814	1,701**	CFS
<b>Source: CDEC Daily Reports</b>			

<b>Goodwin Diversion (GDW)</b>			
Inflow (Tulloch Dam):	896	1,782	CFS
Release to Stanislaus River (S-98):	952	870	CFS
Release to OID (JT Main):	336	725	CFS
Release to SSJID (SO Main):	165	323	CFS
Release to SEWD & CSJWCD:	<u>31</u>	<u>44</u>	CFS
Total Release	1,484	1,962	CFS
<b>Source: Tri-Dam Operations Daily Report</b>			
<b>Farmington Dam (FRM)</b>			
Diverted to SEWD:	30	55	CFS
Diverted to CSJWCD:	0	0	CFS

<b>Surface Water Used</b>			
Irrigators on New Hogan:	0	17	
Irrigators on New Melones:	0	2	
Out-Of-District Irrigators:	0	0	
DJWWTP Production:	36	44	MGD
North Stockton:	6	11	MGD
South Stockton:	6	7	MGD
Cal Water:	20	21	MGD
City of Stockton DWSP Production:	13	13	MGD

<b>District Ground Water Extraction</b>			
74-01	0	0	GPM
74-02	0	0	GPM
North	620	670	GPM
South	1,530	1,555	GPM
Extraction Well # 1	2,560	2,566	GPM
Extraction Well # 2	<u>3,230</u>	<u>3,180</u>	GPM
Total Well Water Extraction	7,940	7,971	GPM
Total Ground Water Production	11	12	MGD

**Note: \*\*The data reported here is available as of 05/10/26**

**\*The data reported here is available as of 05/11/26**

**All other flow data reported here is preliminary, as of 9:00 a.m. on 05/12/26**

# Bellota Weir Modification Project

## April 2026 Update

### Project Summary

- The Bellota Weir Modification Project is a major infrastructure and habitat restoration effort led by the Stockton East Water District (SEWD) on the Calaveras River near Linden in San Joaquin County, California. It is being undertaken to comply with requirements in SEWD’s Calaveras River Habitat Conservation Plan (HCP) and to replace antiquated infrastructure to convey water to the drinking water plant for City of Stockton, agricultural users, and groundwater recharge. The HCP mandates upgrades to aging diversion facilities to improve fish passage and protect ESA-listed species like the Central Valley steelhead and Chinook salmon.
- Under the HCP and related permitting, the project replaces the existing flashboard dam, temporary fish ladder, and cement sill with modern infrastructure designed to balance water delivery reliability and ecosystem needs. Key components include a new screened diversion intake with multiple cylindrical fish screens, an inflatable Obermeyer gate weir, roughened channel and nature-like rock slope fishways, a fish exclusion structure to prevent entrainment into dead-end channels, and improved conveyance pipelines and access facilities. These features are intended to keep salmonids on suitable outmigration routes, enhance volitional passage both upstream and downstream, and reduce fish entrainment while providing more dependable supply to agricultural and municipal users served by SEWD.
- The project also supports broader water management goals — including groundwater recharge and water quality improvements. Through these upgrades, SEWD aims to modernize aging infrastructure to improve water delivery reliability for Stockton East Water District’s customers while meeting federal and state conservation obligations and enhancing long-term habitat conditions for threatened fish species.



### Project Timeline

Bid opening date:	June 26, 2025	Original completion date:	February 15, 2029
Notice to proceed date:	July 28, 2025	Total approved time extensions:	0 days
Original contract time:	1298 days	Current elapsed contract time (as of April 2026):	276 days
Current completion date:	February 15, 2029	Remaining contract time:	1052 days
Percent work completed:	49.3 %	Percent of time elapsed to date:	21.3 %

## Contractor/Construction Related Items

### Recent Activity

- Working on the Care of Water Season 2 plan. Raised TC-2 sheet piles to divert river flow through the existing Mormon Slough 36” bypass and to Old Calaveras River. Restored irrigation flow to the Old Calaveras River channel.
- Removed a section of the TC-4 coffer dam sheet piles to allow for weir construction at the south area of Mormon Slough to begin. TC-5 sheets piles have been removed.
- Began and completed the excavation to subgrade for the south weir pipe piles and 54” WSP Bellota Conveyance Pipeline.
- Continued formwork, rebar and concrete placement for the Intake and Distribution Structures slabs-on-grade and walls.
- Finished the installation of the 54” WSP pipe pile supports between the Intake Structure and Weir Structure. Continuing the installation of the pipe supports to the pipe piles.
- Modified the south work area entry gates, fencing and site access improvements. There are now two entries into the south work area; the primary entrance is the east gate.
- Engineers completed two sample borings at the south area around the South Diversion Structure.
- Began sloping and benching along the north bank of Mormon Slough and began trenching for the installation of the 54” Sluice Pipeline, manholes, and outfall structure.
- Continued maintenance of water pollution controls (BMPs).
- Continued maintenance of dewatering systems (North Side of Morman Slough)

### Upcoming Activity

- Continued Care of Water, Season 2 activities. Continue to remove the remaining TC-4 coffer dam sheet piles along the centerline of Mormon Slough.
- Begin installation of the 54” WSP Bellota Conveyance Pipeline (PL) (north Side)
- Begin weir pipe piles and pipe supports for the 54” WSP Bellota Conveyance PL (South Side)
- Continue formwork, rebar and concrete placement for the Intake and Distribution Structure walls.
- Begin formwork, rebar and concrete placements and the Fish Ladder area.
- Continue sloping and benching along the north bank of Mormon Slough and continue trenching for the installation of the 54” Sluice Pipeline, manholes, and outlet structure. Begin installation of the 54” sluice pipeline, manholes and outlet structure.
- Begin and complete potholing and subsurface investigations for the South Diversion Structure construction activities.
- Begin installation of dewatering systems for the construction activities at south side of Morman Slough. Continue to maintain the remaining dewatering systems at the north side of Mormon Slough.

## Potential Change Orders

- Permanent Access to Intake Structure
- Differing Site Condition at Old Calaveras River.
- Provide grating cover at South Diversion Structure.
- South Diversion Structure Mag Meter and Vault
- Flowmeter and Manhole (South Diversion Bellota Pipeline)
- Flowmeters and Vault (Calaveras Pipeline)
- Relocate south vehicle entry gate east of South Diversion Structure.
- Modify site lighting.
- Additional 54" FCAs at 54" Bellota Conveyance Pipelines
- Concrete weir modifications to accommodate Obermeyer Gates
- Debris rack and rake cleaner modifications.
- Crane Pad Elevation and Drainage
- 75 kVA transformer relocation to Control Building exterior.

## Approved Change Orders

- Pipe pile interior shear rings
- Additional concrete disposal of debris within the riprap along the bank Mormon Slough
- Eliminate sheet pile walls.
- Pipe Plate Omission
- Permanent Sheet Wall Omission
- Additional Rebar and Concrete in Pipe Pile
- Final Pile Elevations
- Additional concrete demo at weir
- Additional clearing and grubbing at Old Calaveras embankment


# Invoice Tracking

## Construction (Shimmick)

Year	Month	Invoiced	Accumulated Total	Approved Change Orders	Contract Amount Remaining	
2025	August	\$ 4,260,500.00	\$ 4,260,500.00		\$ 46,369,500.00	
	September	\$ 3,112,700.00	\$ 7,373,200.00		\$ 43,256,800.00	
	October	\$ 2,232,050.00	\$ 9,605,250.00		\$ 41,024,750.00	
	November	\$ 2,173,398.70	\$ 11,778,648.70	\$ 48,398.70	\$ 38,899,750.00	
	December	\$ 2,220,500.00	\$ 13,999,148.70		\$ 36,679,250.00	
	2026	January	\$ 1,998,500.00	\$ 15,997,648.70		\$ 34,680,750.00
		February	\$ 3,565,639.00	\$ 19,563,287.70	\$ 755,568.79	\$ 31,870,679.79
		March	\$ 2,906,151.54	\$ 22,469,439.24		\$ 28,964,528.25
		April	\$ 3,052,382.72	\$ 25,521,821.96	\$ 294,499.72	\$ 26,206,645.25
		May				
		June				
		July				
August						
September						
October						
November						
December						

Original Contract Value	Approved Change Orders	New Contract Value	Change Order Percentage of Original Contract Value
\$ 50,630,000.00	\$ 1,098,467.21	\$ 51,728,467.21	2.2%
<b>Change Order Totals</b>			

**Project Completion Status**  
**Bellota Weir Modifications Project**

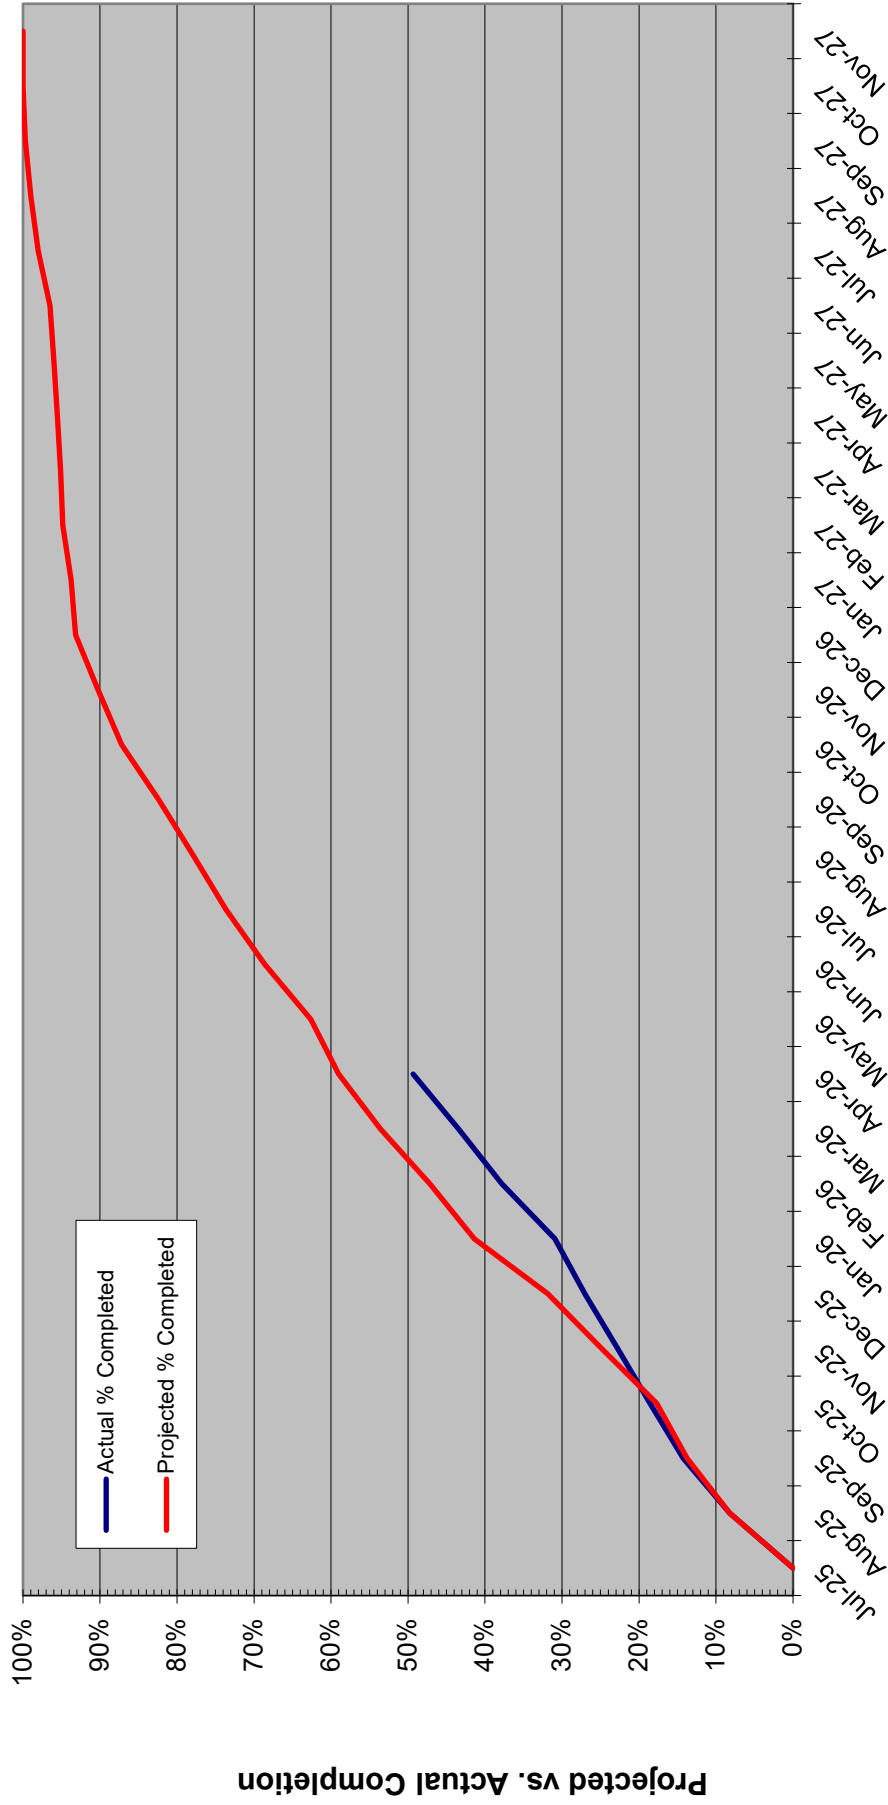

**Project Timeline (Contractor Accelerated Schedule)**

# Progress Photos

